COJB Phase III C
Main Construction Sequence

LEGEND

PHASE 1	PHASE 4	PHASE 7	PHASE 10
PHASE 2	PHASE 5	PHASE 8	PHASE 11
PHASE 3	PHASE 6	PHASE 9	PHASE 12

NOTES:

1. CONSTRUCTION TO BE LIMITED TO A TOTAL OF TWO PHASE BEING CONSTRUCTED AT ANYTIME, INCLUDING SUB PHASES. PHASES AND SUB PHASES MAY NOT BE LOCATED ADJACENT TO ONE ANOTHER. ACCESS TO ALL RESIDENCES AND BUSINESSES MUST BE MAINTAINED AT ALL TIMES.
2. THE 12TH AVE. S. STREET END SHALL BE USED AS THE CONTRACTORS LAY DOWN YARD FOR CONSTRUCTION OPERATIONS AND SHALL BE COMPLETED AS PART OF THE FINAL PHASE (PHASE 12) OF CONSTRUCTION.
3. THE 13TH AVE. S. STREET END SHALL BE PROVIDED AS PARKING AREA FOR RESIDENTS DISPLACED DUE TO CONSTRUCTION OPERATIONS AND SHALL BE COMPLETED AS PART OF PHASE 11 OF CONSTRUCTION.

0 20 100
Feet

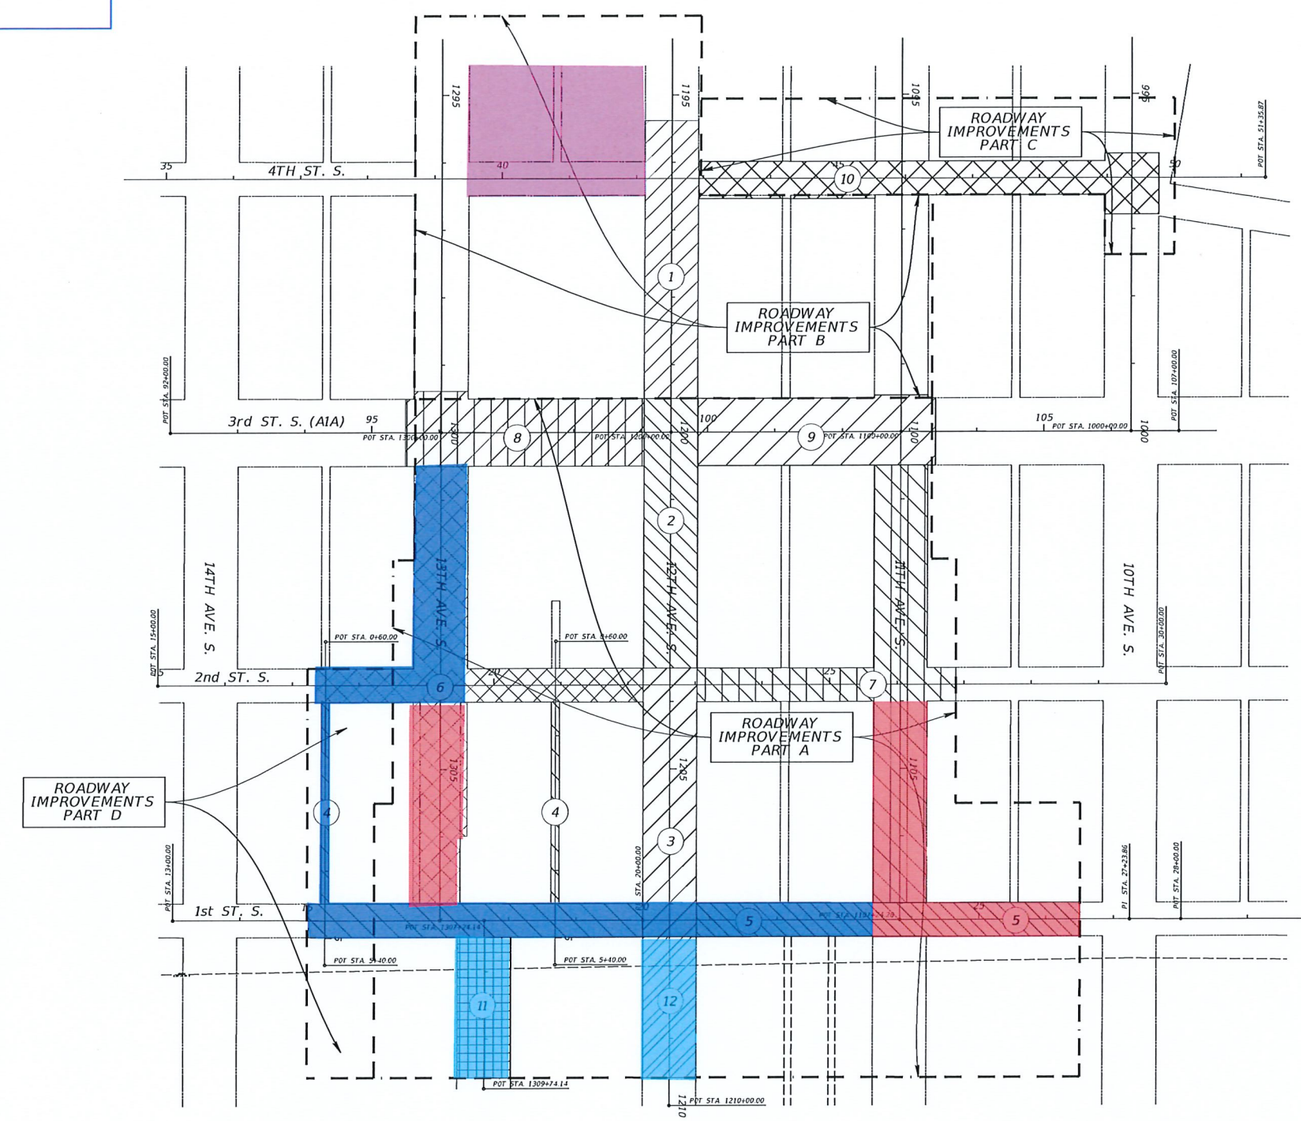

July 2018 - October 2020

April 2020 - October 2020

July 2020 - October 2020

June 2020 - October 2020

RECEIVED BY THE
SEP _ 8 2020
PUBLIC WORKS DEPARTMENT
CITY OF JACKSONVILLE BEACH

REVISIONS							
DATE	DESCRIPTION	DATE	DESCRIPTION	DATE	DESCRIPTION	DATE	DESCRIPTION

MATTHEW N. BOLYARD, P.E.
P.E. LICENSE NUMBER 74635
GAI CONSULTANTS, INC.
1301 RIVERPLACE BOULEVARD - SUITE 900
JACKSONVILLE, FL 32207
CERTIFICATE OF AUTHORIZATION 9951

City of Jacksonville Beach
Department of Public Works

PHASE III C PROJECT 2 IMPROVEMENTS

CONSTRUCTION PHASING PLAN

SHEET NO. 74

10/26/2017 10:49:35 PM P:\GAI\2011\B111180\04 - COJB Phase 3C Project 2\CAD\12th Ave. S. to 11th Ave. S\Strategy\TCPLRD11.DGN
